

Beaver Valley Intermediate Unit – New Horizon School May 2026 Progress Update

Hello Dr. Rosendale, please see the report below for an update on the work completed and what work is anticipated to begin.

Work completed this month:

- Continued miscellaneous carpentry
- Finished brick flashing and brick replacement
- Started brick cleaning and sealing
- Finished drywall installation in all areas and continue drywall tape & finish in 20 Pod, auditorium and corridors.
- Continued HVAC pipe and duct installations
- Started structural steel installation for the new RTU's
- Started roof penetrations and set roof curbs for the RTU's.
- Continued electrical installing lights in Classrooms
- Finished painting walls in the 80, 60, & 40 Pods.
- Started painting door frames.
- Started and finished ceiling grid in 80 Pod, administration offices, nurse office, and the library.
- Finished ceramic tile installation in restrooms of the 80 Pod area and Nurse office.
- Started ceramic tile installation in restrooms of the 40 Pod.
- Formed and placed concrete pad for the new Heating Boilers.
- Removed the old Chiller.
- Started HVAC Pipe and Duct insulation.
- Started and finished VAV box installation.
- Started Plumbing Fixture installation.
- Started reinstalling the Homemaking Room Casework.

Upcoming Work:

- Finish drywall taping in the 20 Pod and corridors.
- Continue HVAC Pipe and Duct insulation.
- Finish HVAC Pipe and Duct installation
- Start HVAC RTU equipment installation.
- Finish HVAC roof curbs & roof patching
- Start storefront/aluminum window replacement work.
- Start flooring installation.
- Finish ceramic wall tile installation in the 40 Pod restrooms
- Start ceramic tile in the 20 Pod restrooms.
- Finish plumbing fixture installation
- Finish reinstallation of the Homemaking Room casework.
- Start HVAC final connections

Schedule:

- The second project schedule update has been issued to subcontractors and is progressing well. The progress is tracking on schedule for substantial completion by 8/14/2026.

Progress Pictures:



80 Pod Classroom



60 Pod Classroom



40 Pod Classroom



80 Pod Restroom



Nurses Office



Nurses Office



Auditorium



20 Pod Classroom



20 Pod Hallway



Library




40 Pod Gym



40 Pod Hallway



Mechanical Room

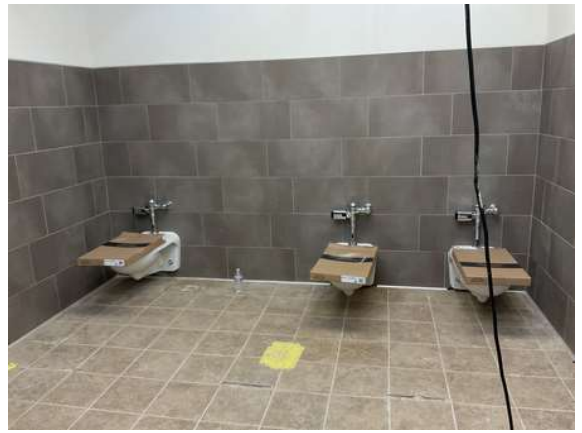

80 Pod Restroom



Brick Cleaning & Sealing



Brick Cleaning & Sealing



Roof Curb for RTU



Roof supports for RTU
