

Beaver Valley Intermediate Unit – New Horizon School July 2026 Progress Update

Hello Dr. Rosendale, please see the report below for an update on the work completed and what work is anticipated to begin.

Work performed this month:

- Continued miscellaneous carpentry
- Continued HVAC pipe and duct installations
- Completed structural steel installation for the new Roof Top Units (RTU's)
- Completed roof penetrations and set roof curbs for the RTU's
- Completed setting of the new RTU's
- Continued installing lights in classrooms and corridors.
- Completed painting corridor walls.
- Continued painting door frames.
- Started and finished ceiling tile installation in 20 Pod, 40 Pod and 60 Pod.
- Started ceiling grid in the corridors
- Started new flooring install in 20 Pod, 40 Pod, 60 Pod classrooms.
- Continued HVAC Pipe and Duct insulation.
- Continued Plumbing Fixture installation.
- Completed reinstalling the Homemaking Room casework and new countertop.
- Continued storefront/aluminum window replacement work.
- Completed restroom partition reinstallation.
- Started final cleaning
- Start moving school furniture and equipment into classrooms
- Start flooring installation in corridors

Upcoming Work:

- Finish HVAC Pipe and Duct installation.
- Finish HVAC RTU final connections.
- Finish HVAC RTU controls.
- Start & finish HVAC Equipment Manufacturer Start-up (RTU's & Boilers)
- Finish storefront/aluminum window detail work.
- Finish flooring installation
- Finish ceiling tile in the cafeteria and corridors.
- Finish plumbing fixture installation.
- Complete final cleaning.
- Finish moving school furniture and equipment into classrooms/offices
- Substantial completion/turn over to the school.

Schedule:

- The schedule is tracking for substantial completion by 8/14/26.
 - *Note: The building occupancy inspection is anticipated for the week of July 27-31.*

Progress Pictures:



Flooring Installation – 20 Pod Classroom



Flooring Installation – Admin Offices



Miscellaneous Carpentry – Auditorium Stage




RTU Crane Lift - Roof



Flooring Installation



Partition & Fixture Reinstallation – Restrooms

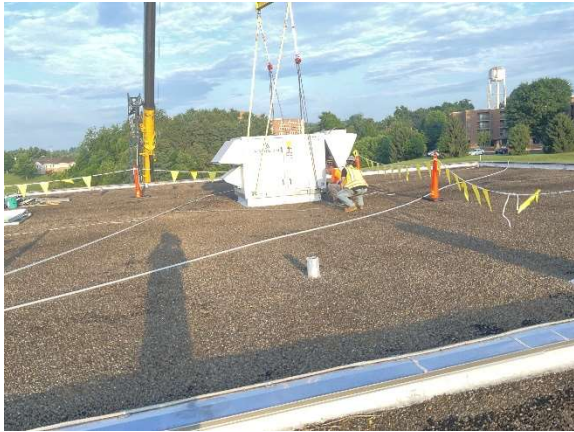

RTU setting - Roof



60 Pod Classroom



New Classroom Casework



80 Pod Hallway



Ceiling Grid - Cafeteria



Homemaking Classroom - Casework Installation
